




















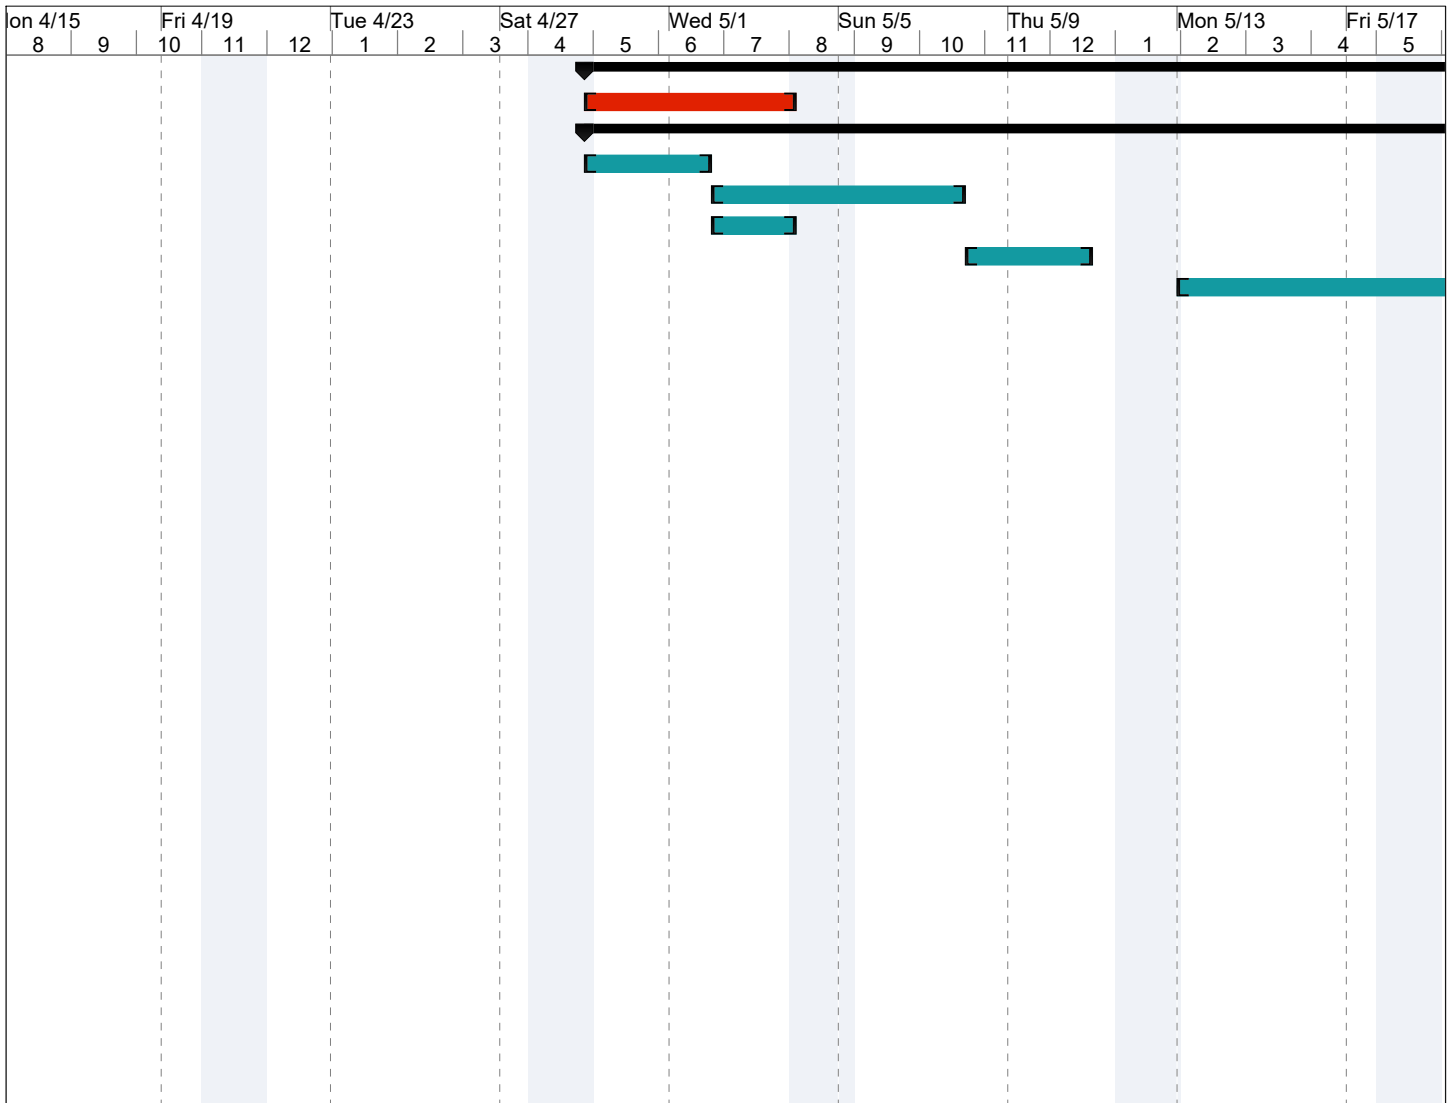


ID	Task Name	Duration	Start	Finish	Sun 4/7			Thu 4/11		Mon 4/
					2	3	4	5	6	7
1	<b>Bedford Street 2019</b>	<b>40 days</b>	<b>Mon 4/29/19</b>	<b>Fri 6/21/19</b>						
2	Remobilize	5 days	Mon 4/29/19	Fri 5/3/19						
3	<b>Water Main</b>	<b>40 days</b>	<b>Mon 4/29/19</b>	<b>Fri 6/21/19</b>						
4	Temp Water Set up	3 days	Mon 4/29/19	Wed 5/1/19						
5	Temp Water testing	4 days	Thu 5/2/19	Tue 5/7/19						
6	Cut-In- Valves	2 days	Thu 5/2/19	Fri 5/3/19						
7	Temp Services	3 days	Wed 5/8/19	Fri 5/10/19						
8	Install Water Main	30 days	Mon 5/13/19	Fri 6/21/19						
9	<b>Sewer</b>	<b>5.5 days</b>	<b>Mon 6/24/19</b>	<b>Mon 7/1/19</b>						
10	Belmeade Rd.	3 days	Mon 6/24/19	Wed 6/26/19						
11	Deerfield Rd.	2.5 days	Thu 6/27/19	Mon 7/1/19						
12	<b>Storm Drain</b>	<b>15 days</b>	<b>Tue 7/2/19</b>	<b>Mon 7/22/19</b>						
13	Belmeade Rd./ Deerfield Rd	7 days	Tue 7/2/19	Wed 7/10/19						
14	Forest Ave	8 days	Thu 7/11/19	Mon 7/22/19						
15	<b>Bedford St. / Durham St. / Baxter Blvd.</b>	<b>28 days</b>	<b>Mon 5/20/19</b>	<b>Wed 6/26/19</b>						
16	Frames and Covers	10 days	Mon 5/20/19	Fri 5/31/19						
17	Misc. Curb and Sidewalk Repair	10 days	Mon 6/3/19	Fri 6/14/19						
18	Biorentention Systems	8 days	Mon 6/17/19	Wed 6/26/19						
19	<b>Box Cut/ Pavement Prep.</b>	<b>9 days</b>	<b>Tue 7/23/19</b>	<b>Fri 8/2/19</b>						
20	Box Cut Forest Ave	5 days	Tue 7/23/19	Mon 7/29/19						
21	Belmeade Neighborhood Pavement Prep	4 days	Tue 7/30/19	Fri 8/2/19						
22	<b>Paving</b>	<b>35.63 days</b>	<b>Thu 6/27/19</b>	<b>Thu 8/15/19</b>						
23	Surface Pave Bedford St.	1 day	Thu 6/27/19	Thu 6/27/19						
24	Surface Pave Durham St.	1 day	Fri 6/28/19	Fri 6/28/19						
25	Pave Binder on Forest Ave.	1 day	Tue 7/30/19	Tue 7/30/19						
26	Pave Binder on Belmeade Neighborhood	1 day	Mon 8/5/19	Mon 8/5/19						
27	Complete Surface Paving	5 days	Sat 8/10/19	Thu 8/15/19						
28	<b>Coastal Road Repair Milling</b>	<b>3 days</b>	<b>Tue 8/6/19</b>	<b>Fri 8/9/19</b>						
29	Forest Ave	1 day	Tue 8/6/19	Wed 8/7/19						
30	Baxter Blvd.	1 day	Wed 8/7/19	Thu 8/8/19						
31	Misc. Milling	1 day	Fri 8/9/19	Fri 8/9/19						
32	<b>Demobilize</b>	<b>7.38 days</b>	<b>Fri 8/16/19</b>	<b>Tue 8/27/19</b>						
33	Clean up, Loam, Seeding, Plantings	5 days	Fri 8/16/19	Thu 8/22/19						
34	Pick Up Signs and Traffic Control	3 days	Thu 8/22/19	Tue 8/27/19						


Project: 2019 Bedford St. Project Sche  
Date: Tue 4/9/19

Task		Manual Task	
Split		Duration-only	
Milestone		Manual Summary Rollup	
Summary		Manual Summary	
Project Summary		Start-only	
External Tasks		Finish-only	
External Milestone		External Tasks	
Inactive Task		External Milestone	
Inactive Milestone		Progress	
Inactive Milestone		Deadline	
Inactive Summary			




Project: 2019 Bedford St. Project Sche  
Date: Tue 4/9/19

Task		Manual Task	
Split		Duration-only	
Milestone		Manual Summary Rollup	
Summary		Manual Summary	
Project Summary		Start-only	
External Tasks		Finish-only	
External Milestone		External Tasks	
Inactive Task		External Milestone	
Inactive Milestone		Progress	
Inactive Milestone		Deadline	
Inactive Summary			

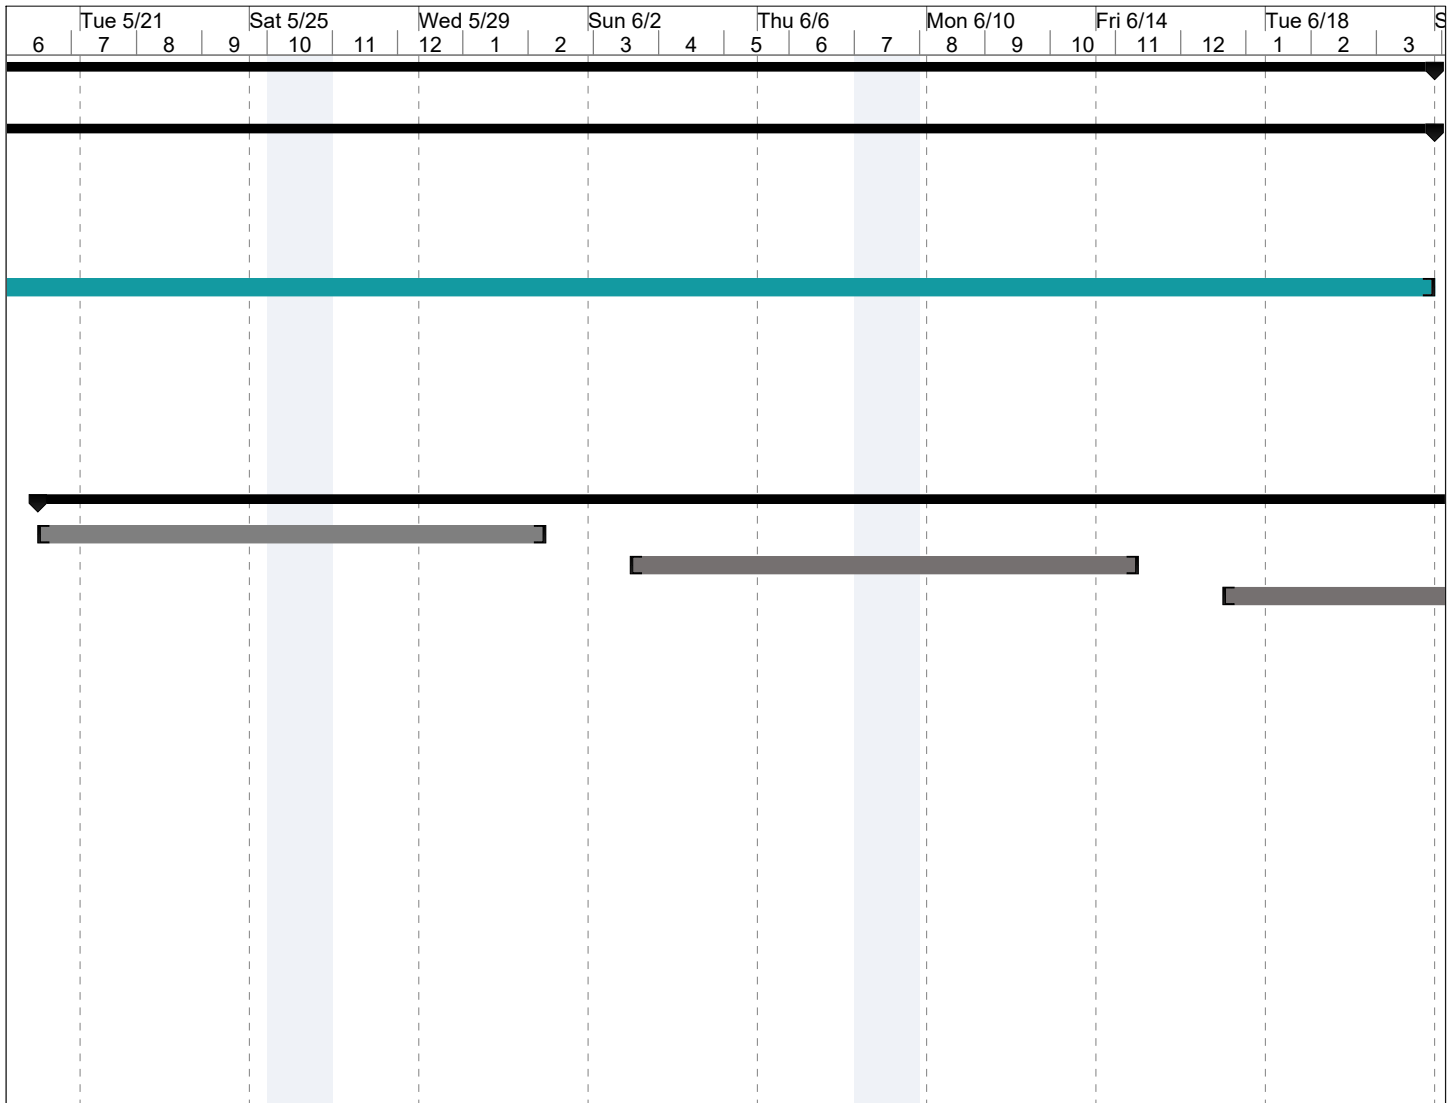


Project: 2019 Bedford St. Project Sche  
Date: Tue 4/9/19

Task		Manual Task	
Split		Duration-only	
Milestone		Manual Summary Rollup	
Summary		Manual Summary	
Project Summary		Start-only	
External Tasks		Finish-only	
External Milestone		External Tasks	
Inactive Task		External Milestone	
Inactive Milestone		Progress	
Inactive Milestone		Deadline	
Inactive Summary			

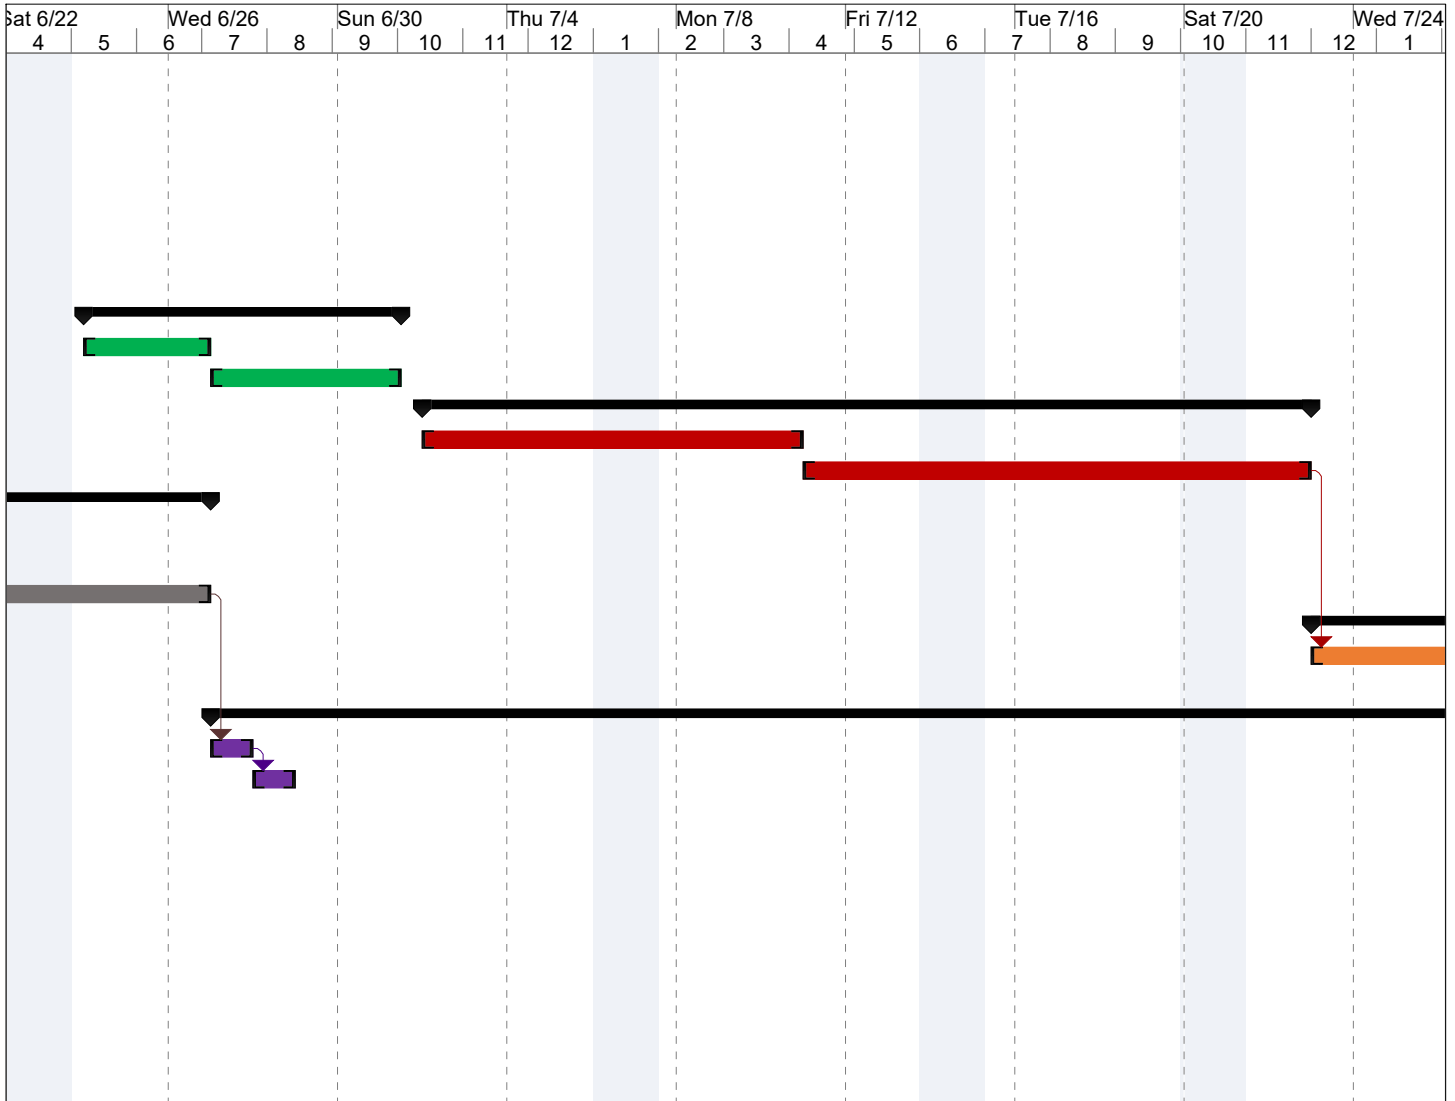

Project: 2019 Bedford St. Project Sche  
Date: Tue 4/9/19

Task		Manual Task	
Split		Duration-only	
Milestone		Manual Summary Rollup	
Summary		Manual Summary	
Project Summary		Start-only	
External Tasks		Finish-only	
External Milestone		External Tasks	
Inactive Task		External Milestone	
Inactive Milestone		Progress	
Inactive Milestone		Deadline	
Inactive Summary			

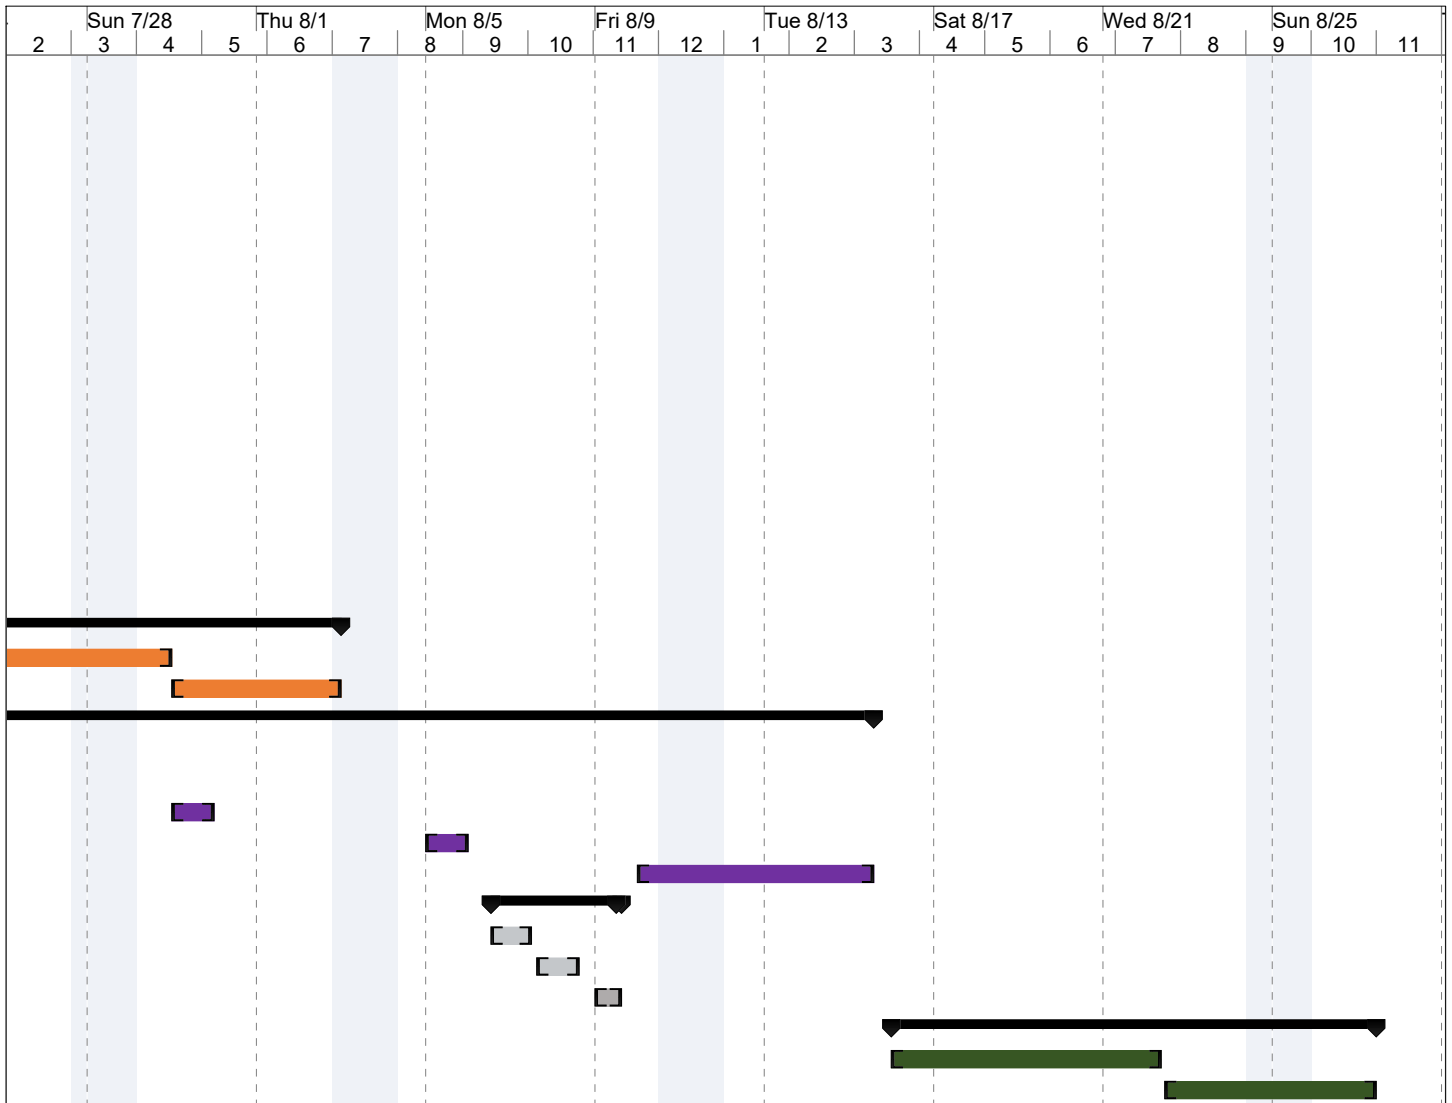

Project: 2019 Bedford St. Project Sche  
Date: Tue 4/9/19

Task		Manual Task	
Split		Duration-only	
Milestone		Manual Summary Rollup	
Summary		Manual Summary	
Project Summary		Start-only	
External Tasks		Finish-only	
External Milestone		External Tasks	
Inactive Task		External Milestone	
Inactive Milestone		Progress	
Inactive Milestone		Deadline	
Inactive Summary			
